COMPLIANCE CHECKLIST

HC-10 — Indoor Air Quality

Riyadh Marina Tower

In Progress | 0 / 3 pts | HC · Health and Comfort | Manual pp.182–185

RATING SYSTEM
Mostadam commercial D+C (2019)

PROJECT STAGE
Design

TARGET LEVEL
Gold

GENERATED
7 Oct 2026, 02:08 GMT+3

> Generated from the project's records in NetZero at the date and time above: the values recorded against each requirement, the files attached against each required document, and the AI's advisory read of those files. Nothing on this document was typed in by hand. A document reads Provided only when a file is attached against it. This is not a log of dated site inspections; where the manual asks for one, it is among the required documents below and the contractor's own sheets are what is attached there.

AIM

To enhance the indoor air quality for building occupants and visitors by minimizing the impact of construction activities, and conducting air quality testing to confirm acceptable indoor air quality.

REQUIRED DOCUMENTS AT A GLANCE

4	1	1	0	1
DOCUMENTS LISTED	DUE AT THIS STAGE	PROVIDED	WITH GAPS (AI)	MISSING

Counts cover the requirements being pursued. Optional requirements nobody has started are listed below but not counted, as on the credit screen.

Requirements and required documents

Project at Design stage

#1 Indoor Air Quality (IAQ) Management Plan

Optional · pursuing | In Progress

Develop and implement an IAQ Management Plan during construction stage and undertake building flush-out prior to occupancy as per the Supporting Guidance.

Recorded value —

	Required document	Stage	State
☐	Specifications and/or contract documents specifying the requirement for the Contractor to develop and implement an IAQ Management Plan and building flush-out plan.	DESIGN	Missing
☐	IAQ Management Plan with all control measures implemented during construction to minimize air pollution, and building flush out evidence.	CONSTRUCTION	Not due yet
☒	Completed IAQ Checklist of all regular inspections performed onsite during construction stage with supporting date-stamped photographic evidence. Dust-Screen-Photo.png 981 B · 7 Oct 2026 (photograph, see below)	CONSTRUCTION	Provided
☐	Report of flush-out activity confirming duration and total outdoor air supplied to the building.	CONSTRUCTION	Not due yet

#2 Indoor Air Quality (IAQ) Testing

Optional · only if pursued

Not Started

A specialist contractor conducts IAQ testing for occupied areas after the end of construction, prior to occupancy. Air contaminants should not exceed the maximum concentration levels specified in the Supporting Guidance.

Recorded value —

Required document	Stage	State
☐ Project specifications confirming the requirement of indoor air quality testing by a specialist IAQ testing agency at the end of construction.	DESIGN	Not pursued yet
☐ IAQ test report confirming the methodology of air sampling and air testing, number of samples taken, concentration of air contaminants and remedial measures undertaken to address any non-compliant measurements (e.g. flush-out and re-testing).	CONSTRUCTION	Not pursued yet
☐ Company profile of the specialized IAQ testing agency confirming qualifications and previous experience.	CONSTRUCTION	Not pursued yet

Photographs 1 image file attached

Every PNG or JPEG attached to this credit, with its upload date and what it was attached against. Other file types are listed above, not shown.

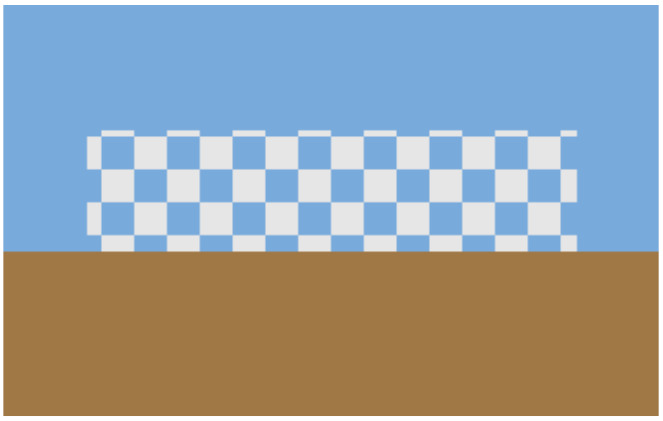

Dust-Screen-Photo.png

Uploaded 7 Oct 2026 · Requirement #1 — Completed IAQ Checklist of all regular inspections performed onsite during construction stage with supporting date-stamped photographic evidence.

What the manual requires the plan to contain

From the credit's supporting guidance (manual pp.182–185).

The IAQ Management Plan must include control measures as per SMACNA IAQ Guidelines for Occupied Buildings under Construction, 2nd Edition-2007, for the following at a minimum:

- [ ] HVAC Protection
- [ ] Source Control
- [ ] Moisture & Mold Control
- [ ] Pathway Interruption
- [ ] Housekeeping
- [ ] Scheduling

Indoor Air Quality Testing

- [ ] The maximum acceptable limits for air contaminants are as follows: Table HC-10.1 Air contaminant limits Contaminant Maximum Concentration Formaldehydes 27 micrograms per m3 PM2.5 Particulates 15 micrograms per m3 PM10 Particulates 150 micrograms per m3 Total Volatile Organic Compounds (TVOC) 500 micrograms per m3
- [ ] Testing protocols for the above contaminants must be compliant with ASTM D5197, ASTM D5466, ASTM D6196, ASTM D6345, and ISO 7708.
- [ ] Air sample testing shall be conducted as follows:
  - [ ] All interior finishes must be installed including doors, paints, carpets and acoustic panels.
  - [ ] Air samples must be collected between 1 and 2 meters from the floor and over a minimum 4-hour period.
  - [ ] The number of sampling points must be at least 1 per 2,500m2 of floor area, or for each continuous floor area.
- [ ] Specialist IAQ testing agency must have at least three years of experience in indoor air quality testing of building projects of a similar type and scale in the GCC.

These boxes are left blank on purpose. They list what the manual requires the plan to contain; whether the uploaded plan covers each one is for the reviewer to judge against the document itself.
